

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

- May 14 – **increase in noise during work hours** – pipe cutting to install new fittings and valves
- Clackamas Fire District # 1, Tualatin Valley Fire & Rescue and Slayden **training on-site at the WTP Saturday May 10, 17 and 24**
- **June 3 update meeting will be replaced with a “Meet the pipeline contractor meeting.”** More information to follow including time & location.
- Pipeline construction update – work scheduled to start on **HDD portion first** (north of Mary S. Young Park), with Mapleton Drive pipeline work to take place next year (Winter 2015). **Site mobilization at HDD staging area to begin early June.**
- **Highway 43 exploratory digging for utilities, mid May – June, 9am-3pm**, some night work within intersections.
- The next public tour to view construction activity at the WTP will be held on Thurs. May 22 at 10 a.m. Sign-up in advance to reserve a spot by email, phone or at the bi-monthly meetings.

Shoring roof support for the clearwell



Project hotline reminder: 503-697-6502

You can also email the project team at lotwater@ci.oswego.or.us or visit LoTigardWater.org

Water Treatment Plant Upgrade Good Neighbor Update – 5-6-14




Slayden's Look Ahead

After-Hours or Weekend Work

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm.

May 5 - 10

- Continue pouring concrete for overflow slabs and shoring roof support for the clearwell
- Continue forming and pouring walls for ballasted flocculation, and begin shoring roof support
- Continue pouring walls for solids storage tank and gravity thickener
- Begin forming slabs in chemical building and mechanical dewatering
- Excavate for new piping – preparation for May 14 work

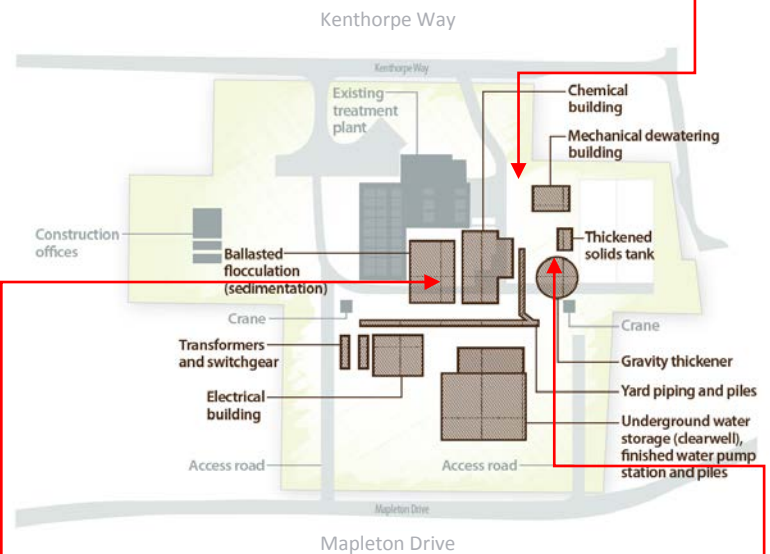

May 12 - 17

- Continue work in ballasted flocculation, solids storage tank, gravity thickener, chemical building and mechanical dewatering, as listed above.
- Begin installing connections and fittings for new temporary supply pipe. **Increase in noise during pipe cutting on May 14** during work hours.

May 19 - 24

- Continue shoring roof support for the ballasted floc.
- Continue pouring walls for gravity thickener
