

Coluccio's HDD Pipeline Look Ahead

June 30 – July 3

- Continue mobilizing equipment, pipe casing, materials on site
- Start installing 60-inch pipe casing using a pressurized hammer, known as pipe ramming – **very noisy during work hours for 1-3 hour periods.** The contractor will start the noisiest work after 9am.
- Continue welding 20 ft casing lengths together

July 7 – 12

- Continue installing 60-inch pipe casing using a pressurized hammer– **very noisy during work hours for 1-3 hour periods.** The contractor will start the noisiest work after 9am.
- Continue welding casing lengths together

Work hours:

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm. **No work on Fourth of July weekend.**

Other work:

- Highway 43 exploratory digging for utilities, complete. Survey work along the roadway now complete.




Signage and information kiosk installed at the HDD site

Slayden's WTP Look Ahead

June 30 – July 3

- Continue pouring slabs for the clearwell roof
- Continue pouring walls for ballasted flocculation, and shoring roof support
- Begin installing shoring roof support for solids storage tank
- Continue water testing the gravity thickener building and applying waterproof coatings
- Continue forming, installing rebar and pouring slabs in chemical building
- Continue installing conduit, rebar and forming for electrical building slabs, some backfilling
- Begin excavating and installing slide rail shoring for 48" overflow pipe, near chemical building
- Install auger cast piles for 48" overflow pipe

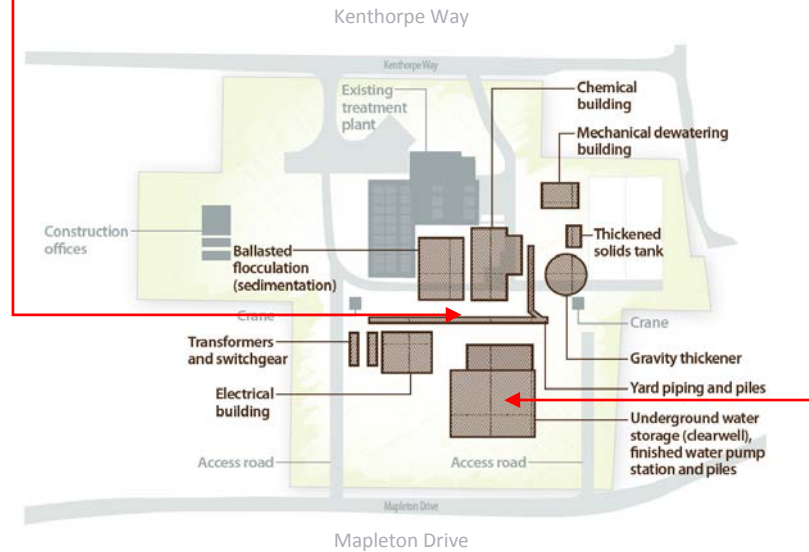

July 7 - 12

- Continue work in the clearwell, ballasted flocculation, solids storage tank, 48" overflow pipe and gravity thickener, as listed above

Work hours:

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm. **No work on Fourth of July weekend.**

More information?

Visit lotigardwater.org, email lotwater@ci.oswego.or.us or call 503-697-6502
