

Coluccio's HDD Pipeline Look Ahead

Crews completed first pilot hole under the river last week!

August 18-23

- Begin first pass at upsizing the hole for the pipe using a large reamer (drill bit) – noise from the separation tank and equipment on site, some truck traffic

August 25-30

- Continue upsizing the hole for the pipe – noise from the separation tank and equipment on site, some truck traffic

Work hours:

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm.




*Above: Crews working on the solids storage tank at the WTP
Below: Installing drill pipe for the pilot hole at the HDD site*



Slayden's WTP Look Ahead

August 18-23

- Continue installing 30" – 48" piping across the site
- Install under slab piping, conduit and slabs for finished water pump station
- Continue concrete pours for the ballasted flocculation, chemical building, electrical building and gravity thickener. Truck traffic will continue with material deliveries and increase during concrete pouring.
- Begin excavating and installing secondary power feed for the plant – between Kenthorpe Way plant entrance and the center of the site
- Remove shoring support for the clearwell roof
- Continue water/leak testing the solids storage tank and apply coatings

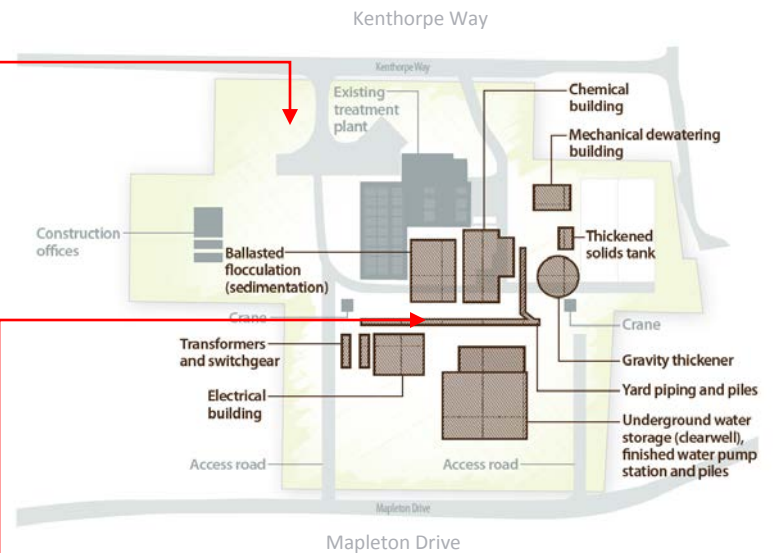

August 25-30

- Continue excavating and installing secondary power feed for the plant
- Continue work as listed above on the solids storage tank, clearwell, finished water pump station, electrical building, chemical building, piping and ballasted flocculation.

Work hours:

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm. No work on Monday, September 1.

More information?

Visit lotigardwater.org, email lotwater@ci.oswego.or.us or call 503-697-6502
