

Coluccio's HDD Pipeline Look Ahead

August 4 - 9

- Mobilize and set up a different steering tool (gyroscope)
- Continue drilling the first pilot hole under the river – noise from the separation tank and equipment on site, some truck traffic

August 11 - 16

- Continue drilling the first pilot hole under the river – noise from the separation tank and equipment on site, some truck traffic

Work hours:

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm.



Forming walls for the Mechanical Dewatering building.




Separating solids and drilling fluid at the solids separation tank at the HDD site

Slayden's WTP Look Ahead

August 4 - 9

- Begin drilling auger cast piles for the finished water pump station
- Continue forming shoring roof support for the ballasted flocculation and mechanical dewatering building
- Begin water/leak testing the solids storage tank
- Continue installing mechanical equipment for the gravity thickener tank
- Continue forming and pouring base slabs for electrical and chemical building
- Backfill area and install auger cast piles for Liquid Oxygen storage tank

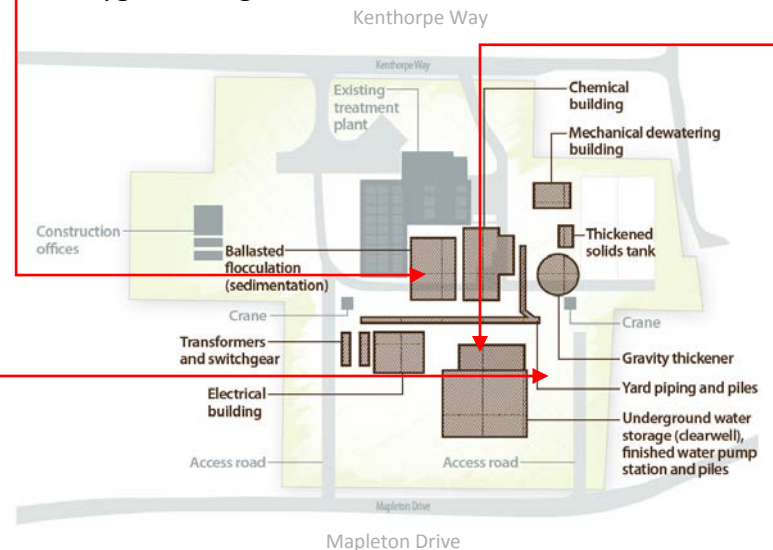

August 11 - 16

- Begin drilling auger cast piles for miscellaneous 30"-42" piping
- Continue work in the clearwell, ballasted flocculation, solids storage tank, and gravity thickener, as listed above

Work hours:

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm.

More information?

Visit lotigardwater.org, email lotwater@ci.oswego.or.us or call 503-697-6502
