

Water Treatment Plant Upgrade Good Neighbor Update – 9/19/13

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

["Work Underway" Webpage](#)

The Work Underway webpage provides the latest construction news project wide.

<http://www.lotigardwater.org/?p=work-underway>




An excavator loading soil into haul trucks on Tuesday 9/17/13

Project Phone Number Reminder!

503-697-6502

If it is outside of M-F 8 am to 5 pm, remember to press 1 to connect to the non-emergency dispatch number, or dial 503-635-0250. Only dial 911 if it is a life or property emergency.

You can also email the project team at lotwater@ci.oswego.or.us



Christian's Three-Week Look Ahead

After-Hours or Weekend Work

- Some Saturdays from 9:00 a.m. to 5:00 p.m.


September 16 – September 21

- Continue excavating temporary staging area west of sedimentation basins for site offices and parking. Expect dump trucks arriving and leaving site.
- Remove vegetation and place rock in areas where structures or temporary roads will be located.

September 23 – September 28

- Deliver equipment (office trailers, excavators, dumpsters) and set up job site offices to area west of sedimentation basins.
- Begin excavating the underground water storage reservoir (clearwell) to the south of the sedimentation basins. Duration about one month. Expect many dump trucks arriving and leaving site.

Kenthorpe Way

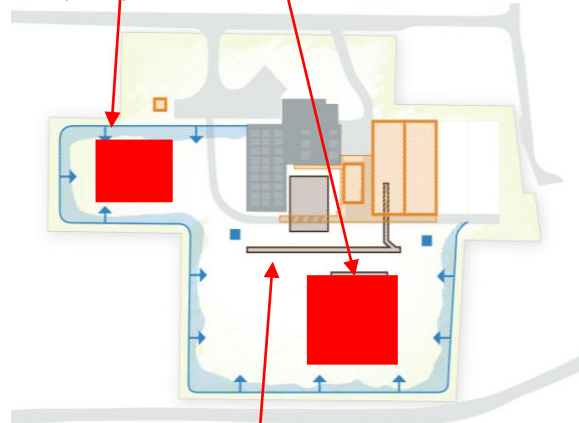

Mapleton Drive

September 30 – October 5

- Begin excavating pipe corridor south of sedimentation basins and north of clearwell.
- Continue excavating clearwell.
