

## Water Treatment Plant Upgrade Good Neighbor Update – 10/01/13

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

### What's New?

#### ["Work Underway" Webpage](#)

The Work Underway webpage provides the latest construction news project wide.

<http://www.lotigardwater.org/?p=work-underway>




*Leveling ground for onsite office trailers on Wednesday 9/25/13*



*A dump truck using the wheel wash before exiting the site on Thursday 9/26/13*

### Project number reminder! **503-697-6502**

If it is outside of M-F 8 am to 5 pm, remember to press 1 to connect to the non-emergency dispatch number, or dial 503-635-0250. Only dial 911 if it is a life or property emergency. You can also email the project team at [lotwater@ci.oswego.or.us](mailto:lotwater@ci.oswego.or.us)



### Slayden's Three-Week Look Ahead

#### After-Hours or Weekend Work

- Some Saturdays from 9:00 a.m. to 5:00 p.m.


#### **September 30 – October 5**

- Complete widening the West Gate entrance off Mapleton.
- Begin pot holing to locate utilities on site.
- Set up temporary job site offices to area west of sedimentation basins.
- Continue excavating the underground water storage reservoir (clearwell) to the south of the sedimentation basins. Expect many dump trucks arriving and leaving site.

#### **October 7 – October 12**

- Continue excavating clearwell and begin installing dewatering system.
- Begin excavating pipe corridor south of sedimentation basins and north of clearwell.
- Continue to deliver equipment to site.

Kenthorpe Way

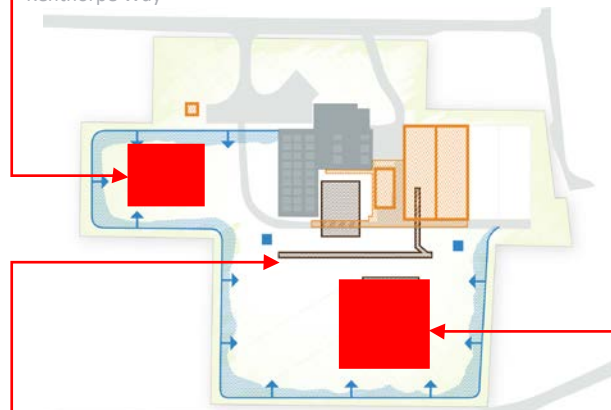

Mapleton Drive

#### **October 14 – October 19**

- Continue excavating pipe corridor and installing dewatering system into clearwell.
- Continue pot holing and temporary piping.
