


## Water Treatment Plant Upgrade Good Neighbor Update – 2-18-14



The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

### What's New?

- Next tour to view construction activity at the WTP is February 27, at 10 am. Sign up by email, phone or at the bi-monthly meetings!
- With the concrete pouring and excavating taking place, the high level of truck traffic will continue.
- Second (westerly) tower crane pile installation will begin late next week.

*Installing sheet piles to support the solids storage tank*



*Preparing the ballasted floc. base prior to pouring concrete*



**Project hotline reminder: [503-697-6502](tel:503-697-6502)**

You can also email the project team at [lotwater@ci.oswego.or.us](mailto:lotwater@ci.oswego.or.us) or visit [LoTigardWater.org](http://LoTigardWater.org)

### Slayden's Three-Week Look Ahead

#### After-Hours or Weekend Work

- Weather permitting, Saturday work February 22 and March 1, from 9 am – 5 pm.


#### February 17 - 22

- Continue forming sump walls in finished water pump station, base slabs and walls in clearwell
- Begin excavating for new solids storage tank and gravity thickener
- Continue forming base slabs for ballasted floc.
- Finish backfilling the finished water pump station in clearwell

#### February 24 – March 1

- Continue forming slab and walls for clearwell
- Continue forming base slabs for ballasted floc.
- Continue excavating for solids storage tank and gravity thickener
- Begin installing auger cast piles for gravity thickener
- Prepare tower crane foundation & begin installing westerly tower crane auger cast piles

Kenthorpe Way

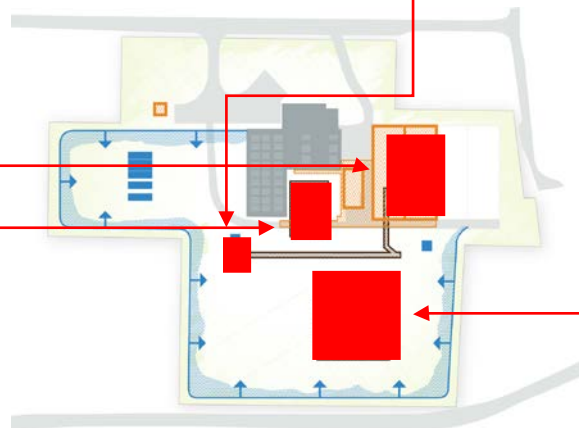

Mapleton Drive

#### March 3 - 8

- Finish base slabs for clearwell
- Continue slabs for ballasted floc.
- Continue installing auger cast piles for gravity thickener and solids storage tank
