


Water Treatment Plant Upgrade Good Neighbor Update – 3-18-14



The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

- Next tour to view construction activity at the WTP is March 27, at 10 am. Sign-up in advance to register a spot by email, phone or at the bi-monthly meetings!
- The project website has been refreshed – check out the new page about construction activities in West Linn
- Second tower crane will be assembled on-site next week using a 200-ton mobile crane.

Preparing the tower crane foundation



Forming the first of the ballasted floc. walls this week



Project hotline reminder: [503-697-6502](tel:503-697-6502)

You can also email the project team at lotwater@ci.oswego.or.us or visit LoTigardWater.org

Slayden's Three-Week Look Ahead

After-Hours or Weekend Work

- Work hours are M-F 7 am – 7 pm and Saturdays from 9 am – 5 pm.


March 17 - 22

- Continue pouring concrete for the walls and columns of the clearwell
- Begin forming shoring support for clearwell roof
- Continue forming walls for ballasted floc. building
- Continue installing auger cast piles for gravity thickener and chemical building

March 24 - 29

- Begin tower crane assembly – large equipment to arrive on site early next week
- Continue pouring concrete for the walls and columns of the clearwell
- Continue forming shoring support for clearwell roof
- Continue forming walls for ballasted floc. building
- Continue installing auger cast piles for gravity thickener and chemical building

Kenthorpe Way

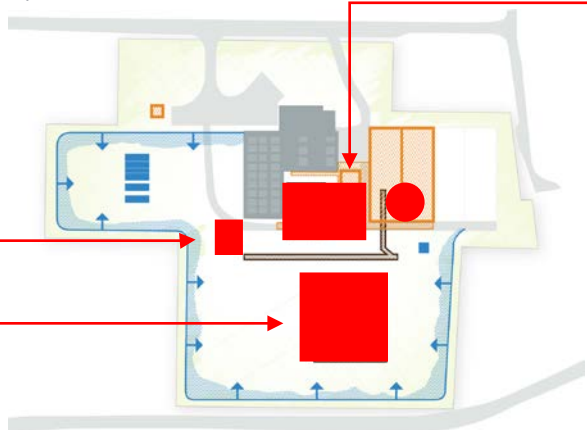

Mapleton Drive

March 31 – April 5

- Install underslab plumbing for chemical building
- Install auger cast piles for mechanical dewatering
- Continue forming walls and columns for clearwell and ballasted floc. building
