

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

- The second tower crane was assembled last week
- The March public tour to view construction activity at the WTP was well attended last week. Sign-up in advance to register a spot by email, phone or at the bi-monthly meetings – next tour is Thursday April 24 at 10 a.m.
- Last week was the first full week with the 5-person crew working until 7:00 p.m.



Assembling the second tower crane last week



Tour attendees viewing a concrete pour in the ballasted flocc.

Project hotline reminder: 503-697-6502

You can also email the project team at lotwater@ci.oswego.or.us or visit LoTigardWater.org

Water Treatment Plant Upgrade Good Neighbor Update – 4-1-14



Slayden's Three-Week Look Ahead

After-Hours or Weekend Work

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm.


March 31 – April 5

- Continue pouring concrete for the walls and columns of the clearwell and ballasted flocc.
- Begin backfilling and compacting fill on southside access and ramp into clearwell – near Mapleton Dr
- Begin forming and pouring slabs for solids storage tank
- Continue installing auger cast piles for chemical building and mechanical dewatering
- Begin installing underslab plumbing and electrical for chemical building

April 7 - 12

- Begin installing conduit for solids storage area
- Continue pouring concrete for the walls and columns of the clearwell and ballasted flocc.
- Continue backfilling and compacting fill on southside access and ramp into clearwell – near Mapleton Dr
- Continue installing auger cast piles for mechanical dewatering

Kenthorpe Way

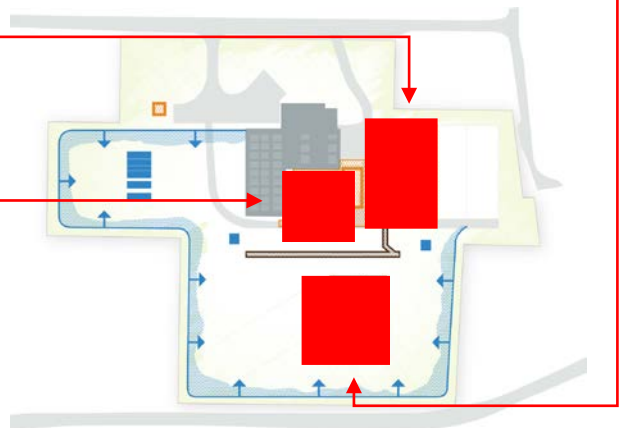

Mapleton Drive

March 31 – April 5

- Continue slabs for solids storage tank
- Continue placing walls and columns of clearwell and ballasted flocc.
