

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

- The next public tour to view construction activity at the WTP will be held on Thurs. April 24 at 10 a.m. Sign-up in advance to reserve a spot by email, phone or at the bi-monthly meetings.
- There will be no work occurring next Saturday, April 26.
- Walls and columns in the clearwell should be complete by the end of April!



Drilling auger cast piles for the electrical building




Vibratory rolling compactor compressing fill south of clearwell

Project hotline reminder: [503-697-6502](tel:503-697-6502)

You can also email the project team at lotwater@ci.oswego.or.us or visit LoTigardWater.org

Water Treatment Plant Upgrade Good Neighbor Update – 4-15-14




Slayden's Look Ahead

After-Hours or Weekend Work

- Work hours are M-F, 7 am – 7 pm and Saturdays from 9 am – 5 pm. No work on Saturday, April 26.

April 14 - 19

- Continue pouring concrete for the walls and columns and shoring roof support for the ballasted floc. and clearwell
- Continue backfilling and compacting fill south of site near Mapleton Dr & northeast of site near wheel wash and mechanical dewatering building
- Continue forming and pouring slabs for solids storage tank and gravity thickener
- Continue drilling auger cast piles for electrical building and chemical building

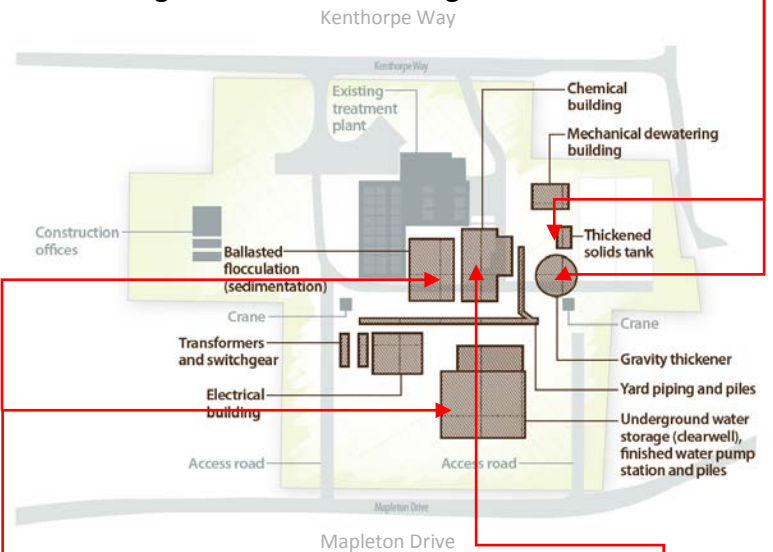

April 21 - 25

- Continue pouring concrete for the walls and columns and shoring roof support for the ballasted floc. and clearwell
- Continue forming and pouring walls for solids storage tank and gravity thickener
- Begin forming slabs for chemical building and mechanical dewatering

April 28 – May 3

- Continue slabs for chemical and mechanical dewatering
- Continue pouring walls for bal. floc. and clearwell
