

Water Treatment Plant Upgrade Good Neighbor Update – 9/5/13

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

"Work Underway" Webpage

The Work Underway webpage provides the latest construction news project wide.

<http://www.lotigardwater.org/?p=work-underway>

Introducing: Katy Fulton


...Your new neighborhood liaison.

Katy Fulton, Citizen Information Specialist
503-697-6502, lotwater@ci.oswego.or.us

Project Phone Number Reminder!

503-697-6502

If it is outside of M-F 8am to 5 pm, remember to press 1 to connect to the non-emergency dispatch number, or dial 503-635-0250. Only dial 911 if it is a life or property emergency.



Christian's Three-Week Look Ahead

After-Hours or Weekend Work


- None

September 3 – September 6

- Surveying and settlement monitoring

September 9 – September 13

- Deliver excavation equipment (forklift, excavators, trackhoes)
- Excavate temporary staging area west of sedimentation basins for construction trailers and parking. One week in duration, expect dump truck trips arriving/leaving site.

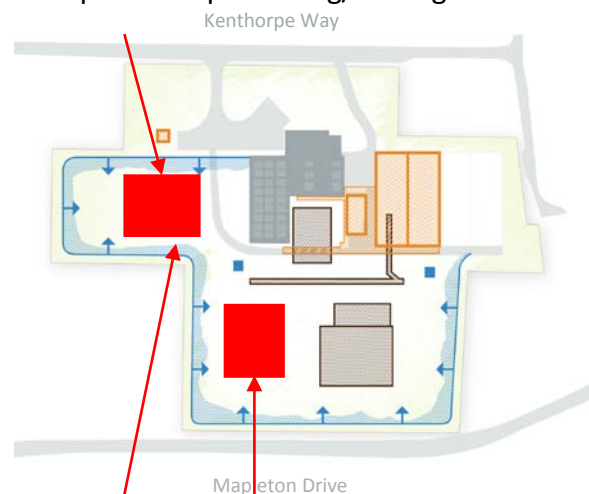

September 16 – September 20

- Deliver and set up job site offices to area west of sedimentation basins
- Remove vegetation/place rock in areas where structures or temporary roads will be located.
- Begin excavation for the underground water storage reservoir (clearwell). Duration is about one month. Expect many dump trucks arriving/leaving site.
