

Water Treatment Plant Upgrade Good Neighbor Update – 11/19/13

The Lake Oswego Tigard Water Partnership is committed to keeping plant neighbors and customers up-to-date on construction progress.

What's New?

- 2" overlay paving of pothole on Old River Drive, between Kenthorpe and Cedaroak scheduled for week of November 18, weather permitting.
- Permanent vibration monitoring equipment placed on-site to continually monitor construction activity and ensure no potential for damage to on-site structures or surrounding homes
- Drilling on the auger cast piles for the lagoon overflow pipe started last week. Auger cast piles for tower crane foundation completed.




Steel cage reinforcing for deep piles arrives at the WTP site.



Auger cast pile drilling for overflow piping for lagoons.

Project number reminder! 503-697-6502

If it is outside of M-F 8 am to 5 pm, remember to press 1. You can also email the project team at lotwater@ci.oswego.or.us



Slayden's Three-Week Look Ahead

After-Hours or Weekend Work

- This Saturday, November 23, from 9 am – 5 pm
- No work on Thanksgiving Day, the Day after Thanksgiving or Saturday, November 30


November 18 – November 23

- Excavate and construct access road into clearwell for auger cast pile crane
- Deliver and set-up 100 ton mobile crane on-site
- No scheduled auger cast pile drilling on-site
- Build tower crane's concrete foundation in clearwell

November 25 – November 30

- Begin drilling auger cast piles to support the clearwell and finished water pump station. Expect an increase in noise, vibration during work hours. Duration about a month.
- Excavate trench for temporary pipe near lagoons
- Continue building tower crane concrete foundation
- Continue to deliver materials and equipment to site

Kenthorpe Way

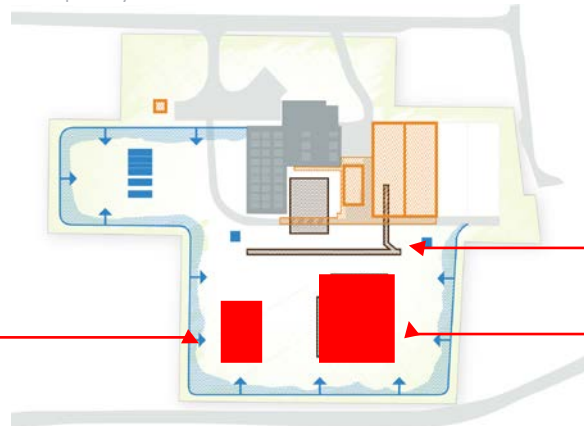

Mapleton Drive

December 2 – December 7

- Continue drilling auger cast piles in clearwell
- Excavate finished water pump station
- Deliver and set up tower crane on-site
